

INDOT
Yeager Road Reconstruction, PH 1

**Yeager Road Reconstruction
PH 1
CHANGE ORDER NOS. 10 and 11**

Original Contract:	\$ 2,319,139.20
Change Order Nos. 1-9	<u>+ 74,815.49</u>
	\$ 2,393,954.69
Change Order No. 10	<u>+ 0.00</u>
	\$ 2,393,954.69
Change Order No. 11	<u>+ 4,245.59</u>
	\$ 2,398,200.28

Approved at a meeting of the West Lafayette Redevelopment Commission held on Wednesday, August 22, 2012 at the West Lafayette City Hall, 609 West Navajo St., West Lafayette, Indiana 47906

WEST LAFAYETTE REDEVELOPMENT COMMISSION

BY: _____
Lawrence T. Oates, President

Attest:

Linda M. Sorensen, Secretary

**INDIANA Department of Transportation
Construction Change Order and Time Extension Summary**

Contract Information

District:CRAWFORDSVILLE
DISTRICT

Contract No.: R -31223

AE:Seef, Erik

Letting Date:11/16/2011

PE/S:Dowty, Chris

Status:Draft

Change Order Information

Date Generated: 00/00/0000

Reason Code: CHANGED COND, Staging Related

Description: Adjusted Completion Date

Change Order No.: 010

Date Approved: 00/00/0000

EWA: N or Force Acct: N

Original Contract Amount	\$ 2,319,139.20	
Current Change Order Amount	\$ 0.00	Percent: 0.000 %
Total Previous Approved Changes	\$ 74,815.49	Percent: 3.226 %
Total Change To-Date	\$ 74,815.49	Percent: 3.226 %
Modified Contract Amount	\$ 2,393,954.69	

Time Extension Information

Date Initiated 00/00/0000

Date Completed 00/00/0000

Original Contract Time

SS Completion Date 11/15/2012 or SS Calendar/Work Days 0

SP Date 00/00/0000 or SP Days

(SS = Standard Specification, SP = Special Provision)

Time Element Description: West Lafayette and INDOT extended the closure of Yeager Road and northbound Northwestern to 75 days rather than the 45 days originally granted for this closure. This results in an earlier completion date by two months by increasing closure time by one month.

Current Time Extension SS Days 0 SP Days 30 SP Days Value \$ 0.00

Previous Time Approved SS Days by AE: _____ DCE: _____ SCE: _____ DDCM: _____

SS Days _____ SP Days Value \$ _____

Revised Contract Time

SS Completion Date 00/00/0000 or SS Calendar/Work Days 0

SS Date 00/00/0000 or SP Days 0

**INDIANA Department of Transportation
Construction Change Order and Time Extension Summary**

Review and Approval Information

Required Approval Authority AE:_____ DCE:_____ SCE:_____ * DDCM:_____ *
(\$ per Change Order) (- LE \$ 250K-) (- LE \$ 750K -) (-- LE \$ 2 M --) (-- GT \$ 2 M --)
(Days per Contract) (50 SS days) (100 SS days) (200 SS Days) (GT 200 SS days)

Verbal Approval Required? Y / N If Y, by _____ Date Issued _____

Total Change To-Date>5%? Y / N If Y , Copy to Program Budget Manager _____

Scope/Design Recommendation Y / N If Y, Referred to Project Manager(PM) _____
Required? Date to PM _____ Date Returned _____

Approval Authority Concurs with PM? Y / N If Y, Concurrence by _____ Date _____
If N,Resolution: Approved _____ Disapproved _____
Resolved by _____ Date _____

LPA Signatures Required? Y / N If Y, Date to LPA _____ Date Returned _____

FHWA Signatures Required? Y / N If Y, Date to FHWA _____ Date Returned _____

* Field Engineer Recommendation (Required for SCE or DDCM Approval)

Field Engineer _____ Date _____

Comments: _____

Contract No:R -31223

INDIANA

Date:07/25/2012

Change Order No:010

Department of Transportation

Page: 3

Contract: R -31223
 Project: State:0600696
 Change Order Nbr: 010
 Change Order Description: Adjusted Completion Date
 Reason Code: CHANGED COND, Staging Related

CLN	PCN	PLN	Item Code	Unit	Unit Price	CO Qty	Comment	Amount Change
Total Value for Change Order 010 = \$ 0.00								

Contract Completion Date Time Adjustment

Original Completion dt: 11/15/2012 Adj compl dt 10/05/2012 Adj No. of Days -62

Explanation: West Lafayette and INDOT extended the closure of Yeager Road and northbound Northwestern to 75 days rather than the 45 days originally granted for this closure. This results in an earlier completion date by two months by increasing closure time by one month.

Milestone Time Adjustment

MileStone Nbr: 02

Milestone Description: CLOSURE TIME

Original Completion dt: 00/00/0000 Adj compl dt 00/00/0000 Adj No. of Days 30

Explanation: West Lafayette and INDOT extended the closure of Yeager Road and northbound Northwestern to 75 days rather than the 45 days originally granted for this closure. This results in an earlier completion date by two months by increasing closure time by one month.

Whereas, the Standard Specifications for this contract provides for such work to be performed, the following change is recommended.

General or Standard Change Order Explanation

At Milestone's request, West Lafayette and INDOT increased the closure of Yeager Road and northbound Northwestern to 75 days from the 45 days originally granted for this closure. This results in an earlier completion date by nearly two months while only increasing the closure time by one month. A safety concern of running traffic next to a drop off exceeding 12" was avoided with this extension. The intermediate completion date remains at 8/31/12.

Change Order Explanation for Specific Line Item

It is the intent of the parties that this change order is full and complete compensation for the work describe above.
Notification and consent to this change order is hereby acknowledged.

Contractor: _____

Signed By: _____

Date: _____

NOTE: Other required State and FHWA signatures will be obtained electronically through the SiteManager system.

Contract No:R -31223
Change Order No:010

INDIANA
Department of Transportation

Date:07/25/2012
Page: 4

APPROVED FOR LOCAL PUBLIC AGENCY

(SIGNATURE)

(TITLE)

(DATE)

(SIGNATURE)

(TITLE)

(DATE)

SUBMITTED FOR CONSIDERATION

PE/S _____

APPROVED FOR INDIANA DEPARTMENT OF TRANSPORATION

Approval Level Name of Approver Date Status

Milestone



May 7, 2012

Dear Mr. Dowty,

I am writing this letter in regards to project R-31223 Yeager Road. Milestone would like to request that Phase 2 (45) day closure be replaced with a (75) day closure. The time extension to this closure will help compensate for 14 calendar days lost, due to utility relocations, (7) days of incimate weather, and early placement of storm structures in front of Pine Manor Apartment complex. The extension of the closure period will allow for the placement of storm structures in advance of original schedule sequence, but will help alleviate an existing condition of standing water in the Pine Manor complex. The new closure period would be from May 14th to July 27th. The closure extension will also allow for a large portion of the project to be built at one time, eliminating several cold joints throughout the project limits. If you have any question please feel free to contact me.

Sincerely,

Chad A. Scott

Chad A. Scott
Project Superintendent
C: 317-694-9934

Cc: Rob Cochran, Conrad Walters, and Job File # 122003

RE: Revised Yeager Schedule

Seef, Erik [ESEEF@indot.IN.gov]

Sent: Tuesday, June 12, 2012 12:53 PM**To:** David Buck [dbuck@westlafayette.in.gov]; Dowty, Chris**Cc:** Ben Anderson [banderson@westlafayette.in.gov]; Wink, Michael [MWink@indot.IN.gov]

Mr. Dowty:

Please proceed with a change order at your earliest convenience to modify the contract completion date from 12-6-12 to 10-5-12. An extension of the road closure period from 45 days to 75 days is also approved. This change also encompasses MOT changes and allows traffic to run on the 53 subbase layer. These changes address the concern with traffic running next to a drop off exceeding 12", and allow the overall project to be completed in shorter duration than originally bid thus having less impact on the public. This approval is associated with West Lafayette's approval in the email chain below.

If you have any comments or questions, do not hesitate to contact me.
Erik Seef

From: David Buck [dbuck@westlafayette.in.gov]
Sent: Thursday, May 31, 2012 2:23 PM
To: Dowty, Chris; Seef, Erik
Cc: Ben Anderson
Subject: RE: Revised Yeager Schedule

Erik,

The City is in agreement with the change in project construction phasing and completion dates as outlined in the revised schedule by Milestone. Chris Dowty with Structurepoint will provide an email with additional explanation & details of the changes.

We support this change because of the following reasons: The duration of overall road closures will be reduced, safety to the public will be increased, the quality of the construction will be improved since several cold joints & matching of phased-curb island construction will be eliminated, and inconveniences to local traffic (apartments and business owners) will be reduced.

Please let me know if you need any additional information from me in order to complete this change to the contract.

Sincerely,

David M. Buck, PE
Public Works Director
Engineering Department
609 West Navajo Street
West Lafayette, Indiana 47906

Phone: 765.775.5130
Fax: 765.775.5249
dbuck@westlafayette.in.gov

Visit us at: www.westlafayette.in.gov

RE: Revised Yeager Schedule

David Buck [dbuck@westlafayette.in.gov]

Sent: Thursday, May 31, 2012 2:23 PM

To: Dowty, Chris; Erik Seef [eseef@indot.in.gov]

Cc: Ben Anderson [banderson@westlafayette.in.gov]

Erik,

The City is in agreement with the change in project construction phasing and completion dates as outlined in the revised schedule by Milestone. Chris Dowty with Structurepoint will provide an email with additional explanation & details of the changes.

We support this change because of the following reasons: The duration of overall road closures will be reduced, safety to the public will be increased, the quality of the construction will be improved since several cold joints & matching of phased-curb island construction will be eliminated, and inconveniences to local traffic (apartments and business owners) will be reduced.

Please let me know if you need any additional information from me in order to complete this change to the contract.

Sincerely,

David M. Buck, PE
Public Works Director
Engineering Department
609 West Navajo Street
West Lafayette, Indiana 47906

Phone: 765.775.5130
Fax: 765.775.5249
dbuck@westlafayette.in.gov

Visit us at: www.westlafayette.in.gov

Working to keep West Lafayette a great community.

This email or any attachment is intended solely for the person(s) addressed. If you are not the intended recipient, be aware that any disclosure, copying, or distribution, or use of this email is prohibited. If you have received this email in error, please notify us immediately by returning it to the sender and deleting this copy from your system. Thank you

-----Original Message-----

From: Dowty, Chris [mailto:CDowty@structurepoint.com]
Sent: Thursday, May 31, 2012 8:58 AM
To: David Buck; Erik Seef
Cc: Ben Anderson
Subject: Revised Yeager Schedule

Attached is the revised schedule for Yeager Road.



Project Meeting - 3/1/12

Date	Start Time	End Time	Next Meeting	Start Time	Minutes Prepared By	Company
May 7, 2012	11:00 AM	12:00PM	May 14, 2012	11:00 AM	Chris Dowty	American Structurepoint, Inc.
Attended By		Location		Next Meeting Location		
Sign in Sheet Attached		West Lafayette City Building		West Lafayette City Building		

Item # Description Status

OLD BUSINESS

- 001.01 SCHEDULE:** Info

Milestone has continued storm installation up Yeager Road. They have also began installing the west half of the storm crossings on Northwestern.
- 001.04 IAW:** Closed

Spectra Tech had a walk-through with Indiana American Water on Friday. They will complete punch list items on Tuesday.
- 001.08 FIELD OFFICE CHANGE ORDER (CO#1):** Open

Milestone has submitted pricing. Erik has reviewed and approved. One change is needed before submitting to West Lafayette
- 002.01 LINE REMOVE (CO #2):**

Pricing has been submitted. Erik will review pricing.
- 002.02 SIGNAL PUCKS:** Open

INDOT will not participate in using pucks rather than loops. West Lafayette will review pricing and decide weather to proceed with pucks and pay the additional costs.
- 002.04 CLAIMS:** Open

Milestone will summarize claims with a cover letter and submit.
- 003.01 CONDUIT FOR MULTI-LANE ROUNDABOUT APPROACHES:** Open

INDOT will not participate in conduit installation for future pedestrian signals. This work will be completed as 100% local funding. Structurepoint will provide a drawing after meeting with West Lafayette about the specifics.
- 003.02 CONCRETE PAD FOR CITY BUS:** Open

City Bus wanting concrete pad connecting sidewalk to back of curb. City will participate if the bus stop is within the project limits. Ben Anderson will meet with City Bus today to clarify where the stop will be located.
- 003.03 HAWK SUBMITTALS FOR LIGHTING AND STRAIN POLES:** Open

Structurepoint has checked and sent back for corrections
- 003.04 PEDESTRIAN TRAFFIC:** Open

Walk has been placed along the west side of Yeager. This work was done on a time and material basis. Milestone has turned in the T&M ticket but will need to revise the equipment pricing to use Federal Highway rental rates. We will also move a "Sidewalk Closed" sign to Sycamore and Anthrop.
- 003.05 MOT ISSUES:** Open

Highway Safety needs to set up the RCA at the south end of Northwestern.

004.01 PHASING:

Open

Milestone will submit a request to close Yeager Road and Northwestern northbound on May 14th citing delays, quality of work building the roundabout and work done outside of phasing to maintain proper drainage as reasoning. The roundabout will need to be open to traffic by July 27, 2012. Milestone will get closure signs up immediately.

004.02 WATER AT PINE MANOR:

Open

Pine Manor has been flooded each time we have had heavy rains. Milestone install drainage structures in front of this property in this phase to establish proper drainage.

004.03 TIE IN AT US 52:

Open

Milestone has noticed a difference in elevation of 0.3' between existing and proposed. Milestone will take shots at the tie in and submit to Structurepoint.

004.04 EXISTING STORM AT US 52:

Open


We will not tie into the existing storm at US 52. We will remove all pipe to the south and brick up the manhole just north of proposed STR 34.

004.05 EROSION CONTROL:

Open

Milestone has installed a check dam on Northwestern. We will monitor this check dam and add another to the north if needed.

Activity Name	Duration	Start	Finish	Bar Chart
122003, R-31223-A, Yeager Road Recon	190	23-Feb-1	25-Sep-1	[Gantt Bar]
Utility Relocation	69	23-Feb	02-Jul	[Gantt Bar]
Phase 1	14	10-Apr	02-Jul	[Gantt Bar]
Ph 2 Closure Yeager and Roundabout	87	14-May	03-Aug	[Gantt Bar]
Start 75 Calendar Day Closure	0	14-May		[Milestone]
Storm Laterals on Yeager and Northwestern Ave.	4	15-May	03-Jul	[Bar]
Northwestern Ave. Pavement Removal and Remaining Yeager	3	21-May	24-May	[Bar]
Common Excavation, Cut to Waste/ Cut to fill	4	21-May	19-Jun	[Bar]
Subgrade Treatment IC under ML	6	21-May	20-Jun	[Bar]
New Item Lime stabilize SB Yeager due to unsuitable mater	3	12-Jun	15-Jun	[Bar]
Finegrade ML	2	20-Jun	22-Jun	[Bar]
Curb inside Roundabout	2	20-Jun	20-Jun	[Bar]
Underdrain Installation	3	25-Jun	27-Jun	[Bar]
2.5" 19mm Base QC/QA 12129 (1460tons)	2	28-Jun	29-Jun	[Bar]
2.25" 19mm OG 15721 (1180 tons)	2	02-Jul-1	03-Jul	[Bar]
Subbase for PCCP	2	02-Jul-1	03-Jul	[Bar]
Curb and Gutter/Modified @ Roundabout Points/WalkWay	5	05-Jul-1	11-Jul	[Bar]
4" 19mm Base QC/QA 12129 (1860tons)	2	12-Jul-1	13-Jul	[Bar]
Colored Conc. Pavement and Pressure Wash	2	12-Jul-1	13-Jul	[Bar]
2.5" 19mm Int. QC/QA 12129 (1300tons) WB & EB Yeager	1	16-Jul-1	16-Jul	[Bar]
Concrete Approaches	2	17-Jul-1	18-Jul	[Bar]
2" HMA Int. Type A 21129 for Drive	1	17-Jul-1	17-Jul	[Bar]
Temp Markings	1	18-Jul-1	18-Jul	[Bar]
July (5days)	5	18-Jul-1	24-Jul	[Bar]
Open Yeager and Roundabout to traffic July 27th Dead line	0		24-Jul	[Milestone]
Sidewalk and Ramps	5	25-Jul-1	31-Jul	[Bar]
Agg. Under path along Yeager	1	01-Aug	01-Aug	[Bar]
Asphalt Path along Yeager	2	02-Aug	03-Aug	[Bar]
Phase 3 SB 231 Outside Lane	67	25-Jul-1	25-Sep	[Gantt Bar]
Pavement Removal	1	25-Jul-1	25-Jul	[Bar]
Common Excavation/Fill	3	26-Jul-1	30-Jul	[Bar]
Subgrade Treatment IC Under ML	1	31-Jul-1	31-Jul	[Bar]
Finegrade ML	1	01-Aug	01-Aug	[Bar]
Underdrain Installation	1	02-Aug	02-Aug	[Bar]
4" 19mm Base QC/QA 12129 (134 tons)	1	03-Aug	03-Aug	[Bar]
2.25" 19mm Int. OG QC/QA 15721 (100 tons)	1	06-Aug	06-Aug	[Bar]
Set Inlets from Phase 1 and Concrete Curbs	2	07-Aug	08-Aug	[Bar]
2.5" 19mm Base QC/QA 12129 (120 tons)	1	09-Aug	09-Aug	[Bar]
2.5" 19mm Base QC/QA 12129 (120 tons)	1	10-Aug	10-Aug	[Bar]
Agg. under Pathway Phase 3 /Finegrade	1	10-Aug	10-Aug	[Bar]
Path Installation Phase 3	1	13-Aug	13-Aug	[Bar]
Backfill Islands and Walks	6	14-Aug	21-Aug	[Bar]
Street Lamps	3	22-Aug	24-Aug	[Bar]
Trees / Seed / Sod	2	27-Aug	28-Aug	[Bar]
1.5" 9.5mm Surface QC/QA (K) 12556 (860 tons) All Phases	2	29-Aug	30-Aug	[Bar]
HMA Surface Type A 21167 (110 tons)	1	31-Aug	31-Aug	[Bar]
Loop Installation	1	04-Sep	04-Sep	[Bar]
Signs, Monuments, Mailboxes, Pvmnt Markings	5	05-Sep	11-Sep	[Bar]
Indement Weather	10	12-Sep	25-Sep	[Bar]
Project Completion By 10/5/12	0		25-Sep	[Milestone]

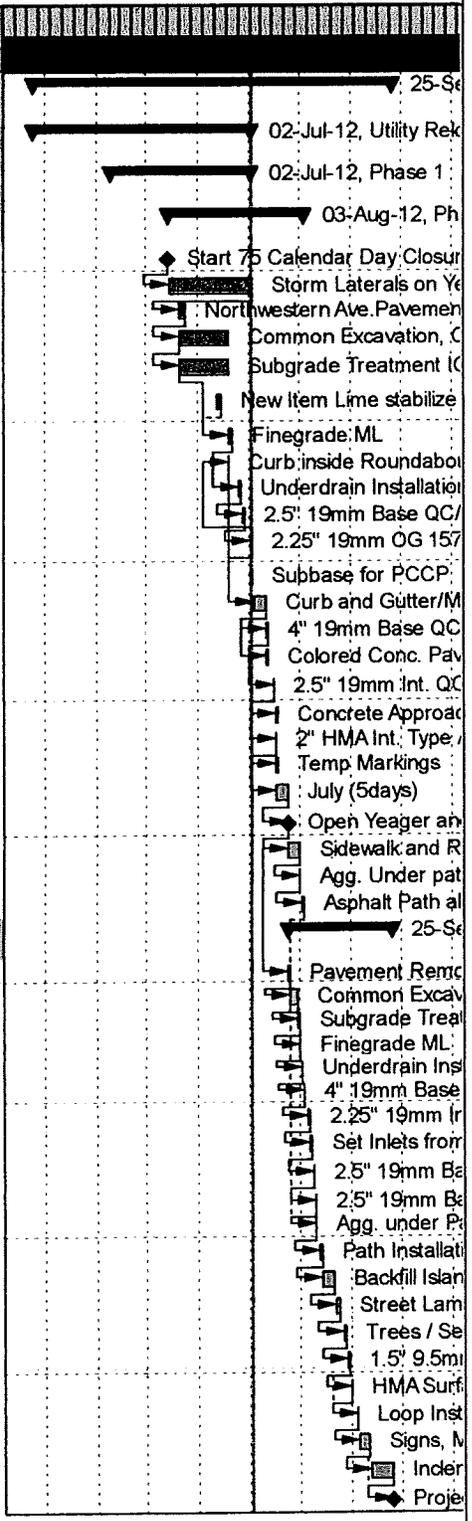

Actual Work
 Critical Remaining Work
 Remaining Work
 Milestone

INDIANA Department of Transportation
Construction Change Order and Time Extension Summary

Contract Information

District:CRAWFORDSVILLE
DISTRICT

Contract No.: R -31223

AE:Seef, Erik

Letting Date:11/16/2011

PE/S:Dowty, Chris

Status:Draft

Change Order Information

Date Generated: 00/00/0000

Change Order No.: 011

Date Approved: 00/00/0000

EWA: Y or Force Acct: N

Reason Code: CHANGED COND, Construction Related

Description: Concrete Wall Removal

Original Contract Amount	\$ 2,319,139.20	
Current Change Order Amount	\$ 4,245.59	Percent: 0.183 %
Total Previous Approved Changes	\$ 74,815.49	Percent: 3.226 %
Total Change To-Date	\$ 79,061.08	Percent: 3.409 %
Modified Contract Amount	\$ 2,398,200.28	

Time Extension Information

Date Initiated 00/00/0000

Date Completed 00/00/0000

Original Contract Time

SS Completion Date 00/00/0000 or SS Calendar/Work Days 0

SP Date 00/00/0000 or SP Days

(SS = Standard Specification, SP = Special Provision)

Time Element Description:

Current Time Extension

SS Days 0 SP Days 0 SP Days Value \$ 0.00

Previous Time Approved

SS Days by AE:_____ DCE:_____ SCE:_____ DDCM:_____

SS Days_____ SP Days Value \$ _____

Revised Contract Time

SS Completion Date 00/00/0000 or SS Calendar/Work Days 0

SS Date 00/00/0000 or SP Days 0

**INDIANA Department of Transportation
Construction Change Order and Time Extension Summary**

Review and Approval Information

Required Approval Authority AE:_____ DCE:_____ SCE:_____ * DDCM:_____ *
(\$ per Change Order) (- LE \$ 250K-) (- LE \$ 750K -) (-- LE \$ 2 M --) (-- GT \$ 2 M --)
(Days per Contract) (50 SS days) (100 SS days) (200 SS Days) (GT 200 SS days)

Verbal Approval Required? Y / N If Y, by _____ Date Issued _____

Total Change To-Date>5%? Y / N If Y , Copy to Program Budget Manager _____

Scope/Design Recommendation Y / N If Y, Referred to Project Manager(PM) _____
Required? Date to PM _____ Date Returned _____

Approval Authority Concurs with PM? Y / N If Y, Concurrence by _____ Date _____
If N,Resolution: Approved _____ Disapproved _____
Resolved by _____ Date _____

LPA Signatures Required? Y / N If Y, Date to LPA _____ Date Returned _____

FHWA Signatures Required? Y / N If Y, Date to FHWA _____ Date Returned _____

* Field Engineer Recommendation (Required for SCE or DDCM Approval)

Field Engineer _____ Date _____

Comments: _____

Contract No:R -31223

INDIANA

Date:07/25/2012

Change Order No:011

Department of Transportation

Page: 3

Contract: R -31223
 Project: 0600696 - State:0600696
 Change Order Nbr: 011
 Change Order Description: Concrete Wall Removal
 Reason Code: CHANGED COND, Construction Related

CLN	PCN	PLN	Item Code	Unit	Unit Price	CO Qty	Comment	Amount Change
0174	0600696	0174	109-04299	DOL	1.000	4245.590	C	Amount:\$ 4,245.59

Item Description: FORCE ACCOUNT WORK
 Supplemental Description1: Asia Wall Removal
 Supplemental Description2: Participating

Total Value for Change Order 011 = \$ 4,245.59

Whereas, the Standard Specifications for this contract provides for such work to be performed, the following change is recommended.

General or Standard Change Order Explanation

Milestone discovered a 4' wall in the existing parking lot of the Asian Market. This wall was marked as curb on the plans. The wall included a footer.

Change Order Explanation for Specific Line Item

It is the intent of the parties that this change order is full and complete compensation for the work describe above.

Notification and consent to this change order is hereby acknowledged.

Contractor: _____

Signed By: _____

Date: _____

NOTE: Other required State and FHWA signatures will be obtained electronically through the SiteManager system.

Contract No:R -31223
Change Order No:011

INDIANA
Department of Transportation

Date:07/25/2012
Page: 4

APPROVED FOR LOCAL PUBLIC AGENCY

(SIGNATURE)

(TITLE)

(DATE)

(SIGNATURE)

(TITLE)

(DATE)

SUBMITTED FOR CONSIDERATION

PE/S _____

APPROVED FOR INDIANA DEPARTMENT OF TRANSPORTATION

Approval Level Name of Approver Date Status



MILESTONE CONTRACTORS, L.P.

Time & Material Work Agreement

(See back for terms and conditions.)

MCLP #: 122003

CUSTOMER NO.: _____

DATE: 06/22/12

DESCRIPTION/SCOPE OF WORK: Removal of Concret wall at the Asia Market

ADDRESS/LOCATION Yeager Road

JOB NO.: R-31223

DATE EFFECTIVE: April 1, 2012 to March 31, 2013

EQUIPMENT RATES DO NOT APPLY TO SNOW REMOVAL

OVERTIME WILL BE CHARGED IN ACCORDANCE WITH UNION AGREEMENTS

EQUIPMENT (OPERATOR NOT INCLUDED)				LABOR		STRAIGHT TIME		TIME + 1/2		DBL. TIME		
DESCRIPTION	HOURLY RATE	HOURS USED	TOTAL (\$)		RATE	HR	RATE	HR	RATE	HR	TOTAL (\$)	
ASPHALT PAVER	\$200.00		\$0.00	LABOR (1)	\$62.00	6.25	\$81.00		\$99.00		\$387.50	
DISTRIBUTOR	\$100.00		\$0.00	OPERATOR (2)	\$79.00	12.50	\$104.00		\$129.00		\$987.50	
BACKHOE w/ Breaker Rental 48.12 Hr	\$48.12	8.00	\$384.96	TEAMSTER	\$68.00		\$90.00		\$112.00		\$0.00	
SCRAPER 613	\$125.00		\$0.00	CARPENTER	\$73.00		\$94.00		\$116.00		\$0.00	
EXCAVATOR LARGE #5489 FHWA	\$168.66	6.25	\$1,054.13	MECHANIC	\$79.00		\$104.00		\$129.00		\$0.00	
EXCAVATOR MEDIUM	\$130.00		\$0.00	FOREMAN (1)	\$64.00	6.25	\$83.00		\$103.00		\$400.00	
EXCAVATOR SMALL	\$90.00		\$0.00	SUPERINTENDENT	\$79.00		\$109.00		\$140.00		\$0.00	
DOZER MEDIUM	\$90.00		\$0.00	HRLY SUPERINTENDE	\$77.00		\$103.00		\$130.00		\$0.00	
DOZER SMALL	\$75.00		\$0.00	MATERIALS & SUPPLIES				QUANTITY	UNIT	PRICE (\$)	TOTAL (\$)	
GRADER LARGE	\$95.00		\$0.00	Concrete Dump Fees				2	Loads	\$ 40.00	\$80.00	
GRADER SMALL	\$50.00		\$0.00								\$0.00	
RUBBER TIRE LOADER	\$85.00		\$0.00								\$0.00	
WHEEL TRACTOR	\$50.00		\$0.00								\$0.00	
STATIC ROLLER	\$35.00		\$0.00								\$0.00	
ROLLER VIBRATORY ASPHALT	\$100.00		\$0.00								\$0.00	
ROLLER VIBRATORY DIRT	\$75.00		\$0.00								\$0.00	
ROLLER SHEEPSFOOT 815	\$125.00		\$0.00	TRUCKING CO.		HOURS		# OF TRUCKS		TOTAL (\$)		
LOWBOY TRACTOR & TRAILER	\$100.00		\$0.00	Spencer Trucking \$81.00Hr		6.50		1		\$526.50		
WATER TRUCK	\$50.00		\$0.00									
SINGLE AXLE FLATBED	\$50.00		\$0.00	SUBCONTRACTORS (Items of work performed)						TOTAL (\$)		
WALK/HAND CONCRETE SAW	\$30.00		\$0.00	ABC Sawcutting (1) 4"x8" Swinghole, (1) 6"x8' Horizontal Cut, & (1) 4'x8' Vertical						\$425.00		
AIR COMPRESSOR/ATTACHMENTS	\$30.00		\$0.00									
GRINDER ATTACHMENTS	\$45.00		\$0.00									
MTL/SKID STEER	\$50.00		\$0.00									
PICKUP TRUCK	\$30.00		\$0.00									
POWER BROOMS	\$50.00		\$0.00									
SIDE PAVER	\$125.00		\$0.00									
VacAll Sweeper Truck.	\$125.00		\$0.00									
			\$0.00									
	Rental Equipment See Note (i)											
	Rental Equipment See Note (i)											

Milestone Contractors, L.P.

Owners Authorized Representative

Time & Material #: _____

Total: \$4,245.59

By: Chad Scott

By: Chris B. Dawdy

Printed: Chad Scott

Printed: CHRIS B. DAWDY

Title: Project Superintendent

Title: Project Supervisor

Revision: (04/17/12)

Office Copy - White

Owner Copy - Yellow

MCLP Superintendent Copy - Pink

THE

Area Plan Commission

of TIPPECANOE COUNTY

20 NORTH 3RD STREET
LAFAYETTE, INDIANA 47901-1209

(765) 423-9242
(765) 423-9154 [FAX]
www.tippecanoe.in.gov/apc

SALLIE DELL FAHEY
EXECUTIVE DIRECTOR

July 31, 2012
Ref No: 2012-235

Dave Buck
City of West Lafayette
609 West Navajo
West Lafayette, IN 47906

REM: Yeager Road
Contract R-31223
Change of Work Orders #10 & #11

Dear Dave:

Attached you will find the signed change order certification for the above referenced project. Change order ten is only an extension of time related to the closure of Yeager Road and northbound Northwestern Avenue. There are no funds involved in the change order. Change order eleven is the removal of a wall and it increases the project cost by \$4,245.59.

As the Greater Lafayette MPO Assistant Director, I hereby authorize these change orders in the amount of \$3,396.47 in STP Funds. Please contact me if you have any questions.

Sincerely,



Sallie Dell Fahey
Executive Director

enclosure

cc. Erik Seef
Brad Rood
Randy Walter

Change Order MPO Certification

Project: Yeager Road
Federal Funds: *STP Group II*
Contract Number: *R-31223*
Change Order Number: *#10 and #11*

Federal Funds Approved: \$3,396.47



Sallie Dell Fahey
Executive Director

7.31.12
Date
