West Lafayette City Hall Inspection

ID	Task Name	Duration	Start	Finish
1	**Option C - DEMOLITION**	**95 days**	**Thu 1/1/15**	**Wed 5/13/15**
2	Permits/Bidding	30 days	Thu 1/1/15	Wed 2/11/15
3	Construction	65 days	Thu 2/12/15	Wed 5/13/15
4				
5	**Option B - CODE/REPAIRS**	**272 days**	**Thu 1/1/15**	**Fri 1/15/16**
6	Design	45 days	Thu 1/1/15	Wed 3/4/15
7	Permits/Bidding	30 days	Thu 3/5/15	Wed 4/15/15
8	Construction	197 days	Thu 4/16/15	Fri 1/15/16
9				
10	**Option A - FULL RENOVATION**	**402 days**	**Thu 1/1/15**	**Fri 7/15/16**
11	Design	132 days	Thu 1/1/15	Fri 7/3/15
12	Permits/Bidding	30 days	Mon 7/6/15	Fri 8/14/15
13	Construction	240 days	Mon 8/17/15	Fri 7/15/16

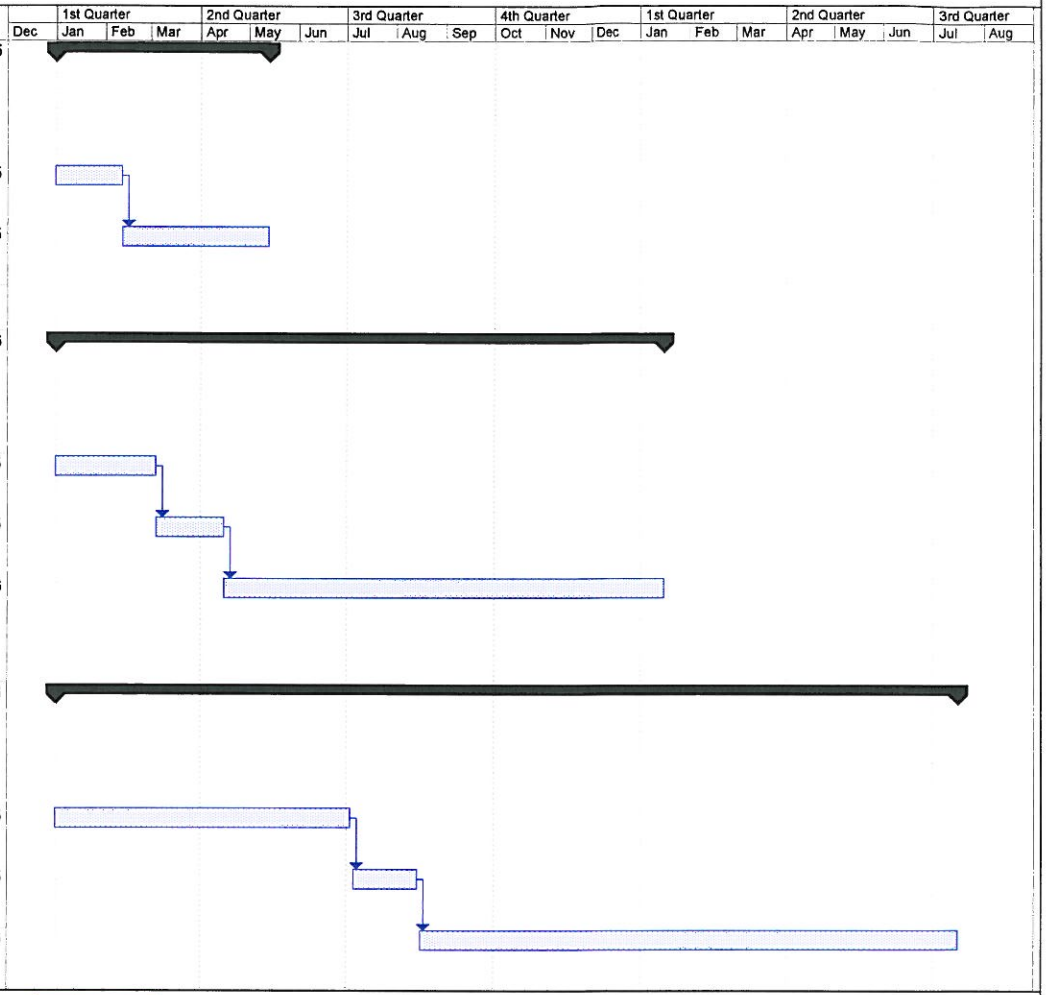

Project: WL City Hall Schedule Option
Date: Mon 11/3/14

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary
